

# PERMASNAP CANTILEVER QUICKLOCKED RADIUS COPING

TAPERED VERSION WITH SADDLE

**IMPORTANT!!!** MUST INDICATE PROPER RADIUS CONDITION BY CIRCLING APPROPRIATE OUTSIDE FACE


PROVIDING A RADIUS  
THE RADIUS MAY BE PROVIDED  
IN ONE OF TWO METHODS:

1.) THE ACTUAL KNOWN RADIUS IS

' FEET  " INCHES MINIMUM OF 3'-0"  
OR


2.) FIELD CONDITION MEASUREMENTS

NOTE: REFER TO ATTACHED WORKSHEET  
FOR FURTHER INFORMATION

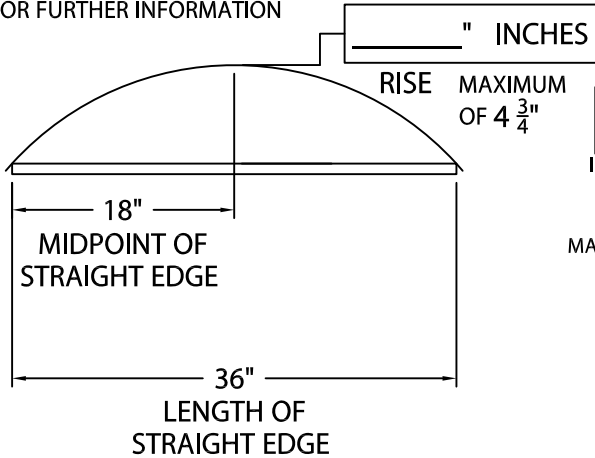

NOTE: CHECK MEASUREMENTS ALONG ENTIRE RADIUS.

DETAIL A

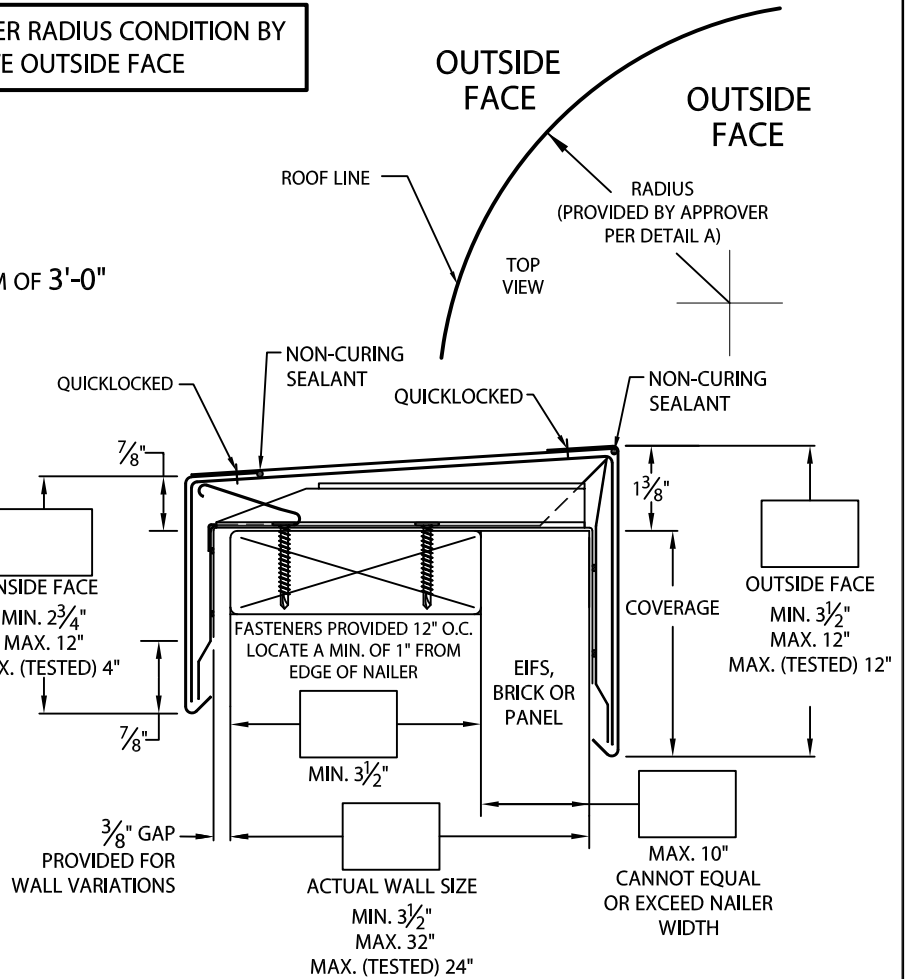

Fabrication will proceed only after receipt of signed print approval.

## Print Approval:

Architect and/or contractor shall verify all dimensions, sizes and quantities. All products to be installed in strict accordance with printed instructions.

Approved by: \_\_\_\_\_

Date: \_\_\_\_\_

PLEASE SPECIFY SUBSTRATE:  
(IF SUBSTRATE INFORMATION IS NOT GIVEN, WOOD SUBSTRATE FASTENERS WILL BE PROVIDED)

WOOD  
 MASONRY  
 METAL

**NOTES:** -- CONCEALED SPLICE PLATES ARE PROVIDED WITH FACTORY APPLIED DUAL NON-CURING SEALANT STRIPS.  
-- FABRICATION OF RADIUS IS FURNISHED UTILIZING A NON-PENETRATING QUICKLOCKED JOINT, THEN FACTORY SEALED WATERTIGHT.

### MATERIALS:

\_\_\_ 24 GA. STEEL  
\_\_\_ .040" ALUMINUM  
\_\_\_ OTHER \_\_\_\_\_

\_\_\_ .050" ALUMINUM  
\_\_\_ .063" ALUMINUM  
COLOR: \_\_\_\_\_  
FINISH: \_\_\_\_\_

### QUANTITIES:

\_\_\_\_\_ LINEAL FEET 4'-0" LENGTHS

PROJECT:

ARCHITECT:

ROOFING CONTRACTOR:

REPRESENTATIVE/DISTRIBUTOR:

**Hickman Edge Systems**

**4 Commerce Way**

**Arden, NC 28704**

**Phone: 828-676-1700**

**www.hickmanedgesystems.com**

DATE: 06/05/24

DRN BY: MLM

CKD BY: MM

SHT.# \_\_\_\_\_ OF \_\_\_\_\_

DWG# 64011-43017

**A**

**HICKMAN**<sup>↑</sup>  
an MTL company
