



PERMASNAP PREMIER PLUS WELDED RADIUS COPING

TAPERED VERSION

IMPORTANT!!! MUST INDICATE PROPER RADIUS CONDITION BY CIRCLING APPROPRIATE OUTSIDE FACE

PROVIDING A RADIUS
THE RADIUS MAY BE PROVIDED
IN ONE OF TWO METHODS:


1.) THE ACTUAL KNOWN RADIUS IS

' FEET " INCHES MINIMUM OF 3'-0"

OR



2.) FIELD CONDITION MEASUREMENTS

NOTE: REFER TO ATTACHED WORKSHEET
FOR FURTHER INFORMATION

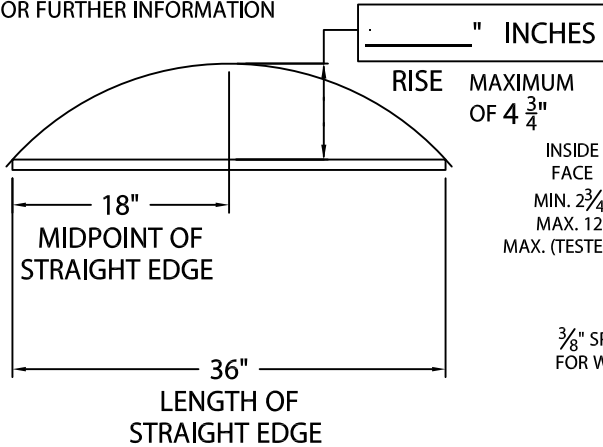

NOTE: CHECK MEASUREMENTS ALONG ENTIRE RADIUS.

DETAIL A

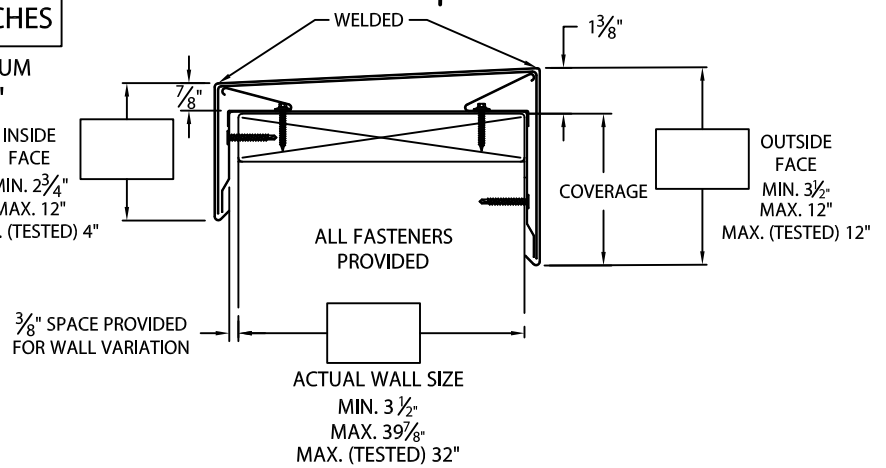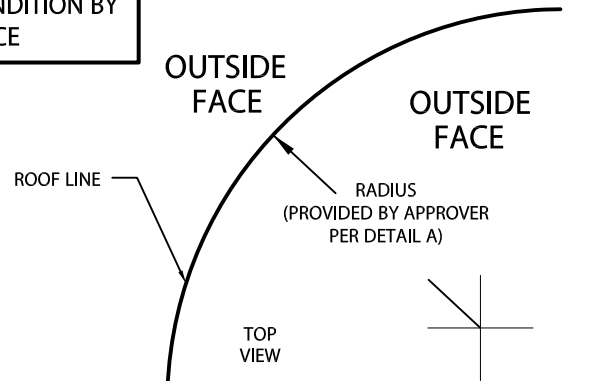

PLEASE SPECIFY SUBSTRATE:
(IF SUBSTRATE INFORMATION
IS NOT GIVEN, WOOD SUBSTRATE
FASTENERS WILL BE PROVIDED)

WOOD
 MASONRY
 METAL

Fabrication will proceed only after receipt of signed print approval.

Print Approval:

Architect and/or contractor shall verify all dimensions, sizes and quantities. All products to be installed in strict accordance with printed instructions.

Approved by: _____

Date: _____

NOTES: -- CONCEALED SPLICE PLATES ARE PROVIDED WITH FACTORY APPLIED DUAL NON-CURING SEALANT STRIPS.

MATERIALS:

TOP - .080" ALUMINUM
SIDES - .063" ALUMINUM
COLOR: _____
FINISH: _____

QUANTITIES:

_____ LINEAL FEET 4'-0" LENGTHS

PROJECT:	Hickman Edge Systems		
ARCHITECT:	4 Commerce Way		
ROOFING CONTRACTOR:	Arden, NC 28704		
REPRESENTATIVE/DISTRIBUTOR:	Phone: 828-676-1700		
	www.hickmanedgesystems.com		
HICKMAN an MTL company	DATE: 08/04/23	SHT.# ____ OF ____	
	DRN BY: MLM		
	CKD BY: MM	DWG# 64011-38593	D
